



**COURSE OVERVIEW PM0092**  
**Risk Management Professional (PMI-RMP)**  
**(PMI Exam Preparation Training)**

**Course Title**

Risk Management Professional (PMI-RMP)  
(PMI Exam Preparation Training)

**Course Date/Venue**

September 27-October 01, 2026/Musandam Meeting  
Room, Royal Tulip Hotel, Muscat, Oman

**Course Reference**

PM0092

**Course Duration/Credits**

Five days/4.0 CEUs/40 PDHs



**Course Description**



***This practical and highly-interactive course includes various practical sessions and exercises. Theory learnt will be applied using our software tools.***

This course is designed to provide participants with a detailed and up-to-date overview of project risk management and to prepare them to pass the PMI-RMP examination in order for them to achieve the PMI-RMP title. The course will give participants with enough knowledge and skills opportunities.



The course will cover the 5 domains comprising the PMI-RMP certification examination. These domains include Risk Strategy & Planning, Risk Identification, Risk Analysis, Risk Response and Monitor & Close Risks.



The course is carefully developed to reflect the best practices that match the training requirements of the Project Management Institute (PMI). The Professional Development Units/Hours (PDUs) or Continuing Education Units (CEUs) awarded to the participants are recognized by the Project Management Institute (PMI) and by the International Association for Continuing Education & Training (IACET-USA).

Further, the course covers the project risk management; the risk management properties, project risk and risk properties; the stakeholder risk attitudes, iterative process, risk process flow and responsibility for project risk management; the project risk management processes, project risk management and project management; the plan risk management, plan risk management inputs, project management plan, project charter, stakeholder register, etc; and the potential risk covering risks inputs, stakeholder register, organizational process assets and tools and techniques for identifying risks.

During this interactive course, participants will learn the information gathering, brainstorming, nominal group technique, delphi technique, interviewing and root cause analysis; the checklist analysis, assumptions analysis, diagramming techniques, flow chart diagram and influence diagramming; the strengths, weaknesses, opportunities and threats (SWOT); the expert judgment, risks outputs, identified risks, potential responses and triggers; the qualitative and quantitative risk analysis process; and the risk responses process and apply control risks.

### **Course Objectives/Outcomes & Benefits for the Participants**

Upon the successful completion of this course, each participant will be able to:-

- Get prepared for the next PMI-RMP exam and have enough knowledge and skills to pass such exam in order to get the PMI certification
- Carryout project risk management and discuss risk management properties, project risk and risk properties
- Explain stakeholder risk attitudes, iterative process, risk process flow and responsibility for project risk management
- Illustrate project risk management processes, project risk management and project management
- Employ plan risk management, plan risk management inputs, project management plan, project charter, stakeholder register, etc
- Identify potential risk covering risks inputs, stakeholder register, organizational process assets and tools and techniques for identifying risks
- Apply information gathering, brainstorming, nominal group technique, delphi technique, interviewing and root cause analysis
- Carryout checklist analysis, assumptions analysis, diagramming techniques, flow chart diagram and influence diagramming
- Define strengths, weaknesses, opportunities and threats (SWOT) and discuss expert judgment, risks outputs, identified risks, potential responses and triggers
- Perform qualitative and quantitative risk analysis process
- Plan risk responses process and apply control risks

### **Exclusive Smart Training Kit - H-STK®**



*Participants of this course will receive the exclusive “Haward Smart Training Kit” (H-STK®). The H-STK® consists of a comprehensive set of technical content which includes **electronic version** of the course materials conveniently saved in a **Tablet PC**.*



### **Who Should Attend**

The course provides an overview of all significant aspects and considerations of risk management for all managers, engineers and supervisors who already have knowledge of project management techniques and tools. Some managers are directly responsible for projects and need to manage risk professionally. Others need to know about pitfalls in risk management when managing project management consultants.

### **Exam Eligibility & Structure**

To be eligible for the PMI-RMP credential, you must meet certain educational and professional experience requirements. All project risk management experience must have been accrued within the last five consecutive years prior to your application submission.

| <b>Educational Background</b>                                                                      | <b>Project Risk Management Experience</b>                                                                                       | <b>Project Risk Management Education</b>                                                |
|----------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------|
| Secondary diploma (high school diploma, associate's degree or global equivalent)                   | At least 36 months spent in the specialized area of professional project risk management within the last five consecutive years | 40 contact hours of formal education in the specialized area of project risk management |
| <b>OR</b>                                                                                          |                                                                                                                                 |                                                                                         |
| Four-year degree (bachelor's degree or global equivalent)                                          | At least 24 months spent in the specialized area of professional project risk management within the last five consecutive years | 30 contact hours of formal education in the specialized area of project risk management |
| <b>OR</b>                                                                                          |                                                                                                                                 |                                                                                         |
| Bachelor's or post-graduate degree from a GAC accredited program (bachelor's or global equivalent) | At least 12 months spent in the specialized area of professional project risk management within the last five consecutive years | 30 contact hours of formal education in the specialized area of project risk management |

### **Training Fee**

**US\$ 5,500** per Delegate + **VAT**. This rate includes H-STK® (Haward Smart Training Kit), buffet lunch, coffee/tea on arrival, morning & afternoon of each day.

### **Exam Fee**

**US\$ 895** per Delegate + **VAT**.

### **Accommodation**

Accommodation is not included in the course fees. However, any accommodation required can be arranged at the time of booking



### Course Certificate(s)

- (1) PMI-RMP certificates will be issued to participants who have successfully passed the PMI-RMP examination.



- (2) Official Transcript of Records will be provided to the successful delegates with the equivalent number of ANSI/IACET accredited Continuing Education Units (CEUs) earned during the course

| * Howard Technology * CEUs * Howard Technology * CEUs * Howard Technology * CEUs * Howard Technology * |                                                                        |                      |                      |       |
|--------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------|----------------------|----------------------|-------|
| Howard Technology Middle East<br>Continuing Professional Development (HTME-CPD)                        |                                                                        |                      |                      |       |
| <b>CEU Official Transcript of Records</b>                                                              |                                                                        |                      |                      |       |
| TOR Issuance Date: 14-Nov-23                                                                           |                                                                        |                      |                      |       |
| HTME No. 74851                                                                                         |                                                                        |                      |                      |       |
| Participant Name: Waleed Al Habeeb                                                                     |                                                                        |                      |                      |       |
| Program Ref.                                                                                           | Program Title                                                          | Program Date         | No. of Contact Hours | CEU's |
| PM0092                                                                                                 | Risk Management Professional (PMI-RMP) (PMI Exam Preparation Training) | November 10-14, 2023 | 40                   | 4.0   |

## **Certificate Accreditations**

Haward's certificates are accredited by the following international accreditation organizations: -

- 

PMI: Project Management Institute

Haward Technology is an **Authorized Training Partner** of the **Project Management Institute (PMI)** (USA). We are strictly complying with the quality requirements and standards of PMI. Haward Technology is approved by PMI to issue contact hours and PDUs for those courses following the PMI requirements in addition to all PMI Project Management courses. Our trainers are Authorized by PMI to deliver the PMI Accredited courses and certification programs. As an Authorized Training Partner, Haward Technology has access to the latest and up-to-date PMI materials and resources available in the field of Project Management that will definitely improve the chances of success for participants attending Haward Technology courses.

The PMI Authorized Training Partner seal is a registered mark of **Project Management Institute, Inc.**

- 

British Accreditation Council (BAC)

Haward Technology is accredited by the British Accreditation Council for Independent Further and Higher Education as an International Centre. Haward's certificates are internationally recognized and accredited by the British Accreditation Council (BAC). BAC is the British accrediting body responsible for setting standards within independent further and higher education sector in the UK and overseas. As a BAC-accredited international centre, Haward Technology meets all of the international higher education criteria and standards set by BAC.

- 

The International Accreditors for Continuing Education and Training (IACET - USA)

Haward Technology is an Authorized Training Provider by the International Accreditors for Continuing Education and Training (IACET), 2201 Cooperative Way, Suite 600, Herndon, VA 20171, USA. In obtaining this authority, Haward Technology has demonstrated that it complies with the **ANSI/IACET 2018-1 Standard** which is widely recognized as the standard of good practice internationally. As a result of our Authorized Provider membership status, Haward Technology is authorized to offer IACET CEUs for its programs that qualify under the **ANSI/IACET 2018-1 Standard**.

Haward Technology's courses meet the professional certification and continuing education requirements for participants seeking **Continuing Education Units (CEUs)** in accordance with the rules & regulations of the International Accreditors for Continuing Education & Training (IACET). IACET is an international authority that evaluates programs according to strict, research-based criteria and guidelines. The CEU is an internationally accepted uniform unit of measurement in qualified courses of continuing education.

Haward Technology Middle East will award **4.0 CEUs** (Continuing Education Units) or **40 PDHs** (Professional Development Hours) for participants who completed the total tuition hours of this program. One CEU is equivalent to ten Professional Development Hours (PDHs) or ten contact hours of the participation in and completion of Haward Technology programs. A permanent record of a participant's involvement and awarding of CEU will be maintained by Haward Technology. Haward Technology will provide a copy of the participant's CEU and PDH Transcript of Records upon request.

## Course Instructor(s)

This course will be conducted by the following instructor(s). However, we have the right to change the course instructor(s) prior to the course date and inform participants accordingly:



**Dr. Chris Le Roux**, PhD, M.Com, B.Com (Hons), PMP, Industrial Psychologist (HPCSA Reg.), PMI-ATP Instructor PMI-PMP, PMI-CAPM Instructor is a **Senior Management Consultant & Project Management Professional** with over **30 years** of combined engineering, managerial, consulting, counseling, and international training experience across Africa, the Middle East, the Gulf region, and Europe. His expertise lies extensively in the areas of **Project & Contracts Management Skills, Project & Construction Management, Project Planning, Scheduling, Cost Control, and Earned Value Management, Project Management (Predictive, Agile, and Hybrid), PMO setup and governance, Project Delivery & Governance Framework, Project Management Practices, Project Management**

**Disciplines, Risk and Contract Management** (including contract development, tendering, dispute resolution, and claims), **Risk Identification Tools & Techniques, Project Life Cycle, Stakeholder Management and Communication, Performance Coaching and Difficult Conversations, Project Management Processes, Project Integration Management, Project Management Plan, Project Work Monitoring & Control, Project Scope Management, Project Time Management, Project Cost Management, Project Quality Management, Quality Assurance, Project Human Resource Management, Project Communications Management, Leadership Orientation Programme, Leadership & Team Development, Psychology of Leadership, Interpersonal Skills & Teamwork, Coaching & Mentoring, Innovation & Creativity, Leadership & Performance Management, Leadership Communication, Leadership Excellence for Senior Management, Supervisory, Leadership, Coaching & Mentoring, Leadership, Communications & Interpersonal Skills, Administrative Leadership Skills, Office Management & Administration Skills, Contract Management, Tender Development, Contract Standards & Laws, Dispute Resolution & Risk Identification, Myers-Briggs Type Indicator (MBTI), Organization Development Consultation, Advanced Debriefing of Emotional Trauma, Interpersonal Motivation, Model Based Interviewing, Coaching & Motivation, Creative Thinking & Problem-Solving Techniques, Emotional Intelligence and Resilience, Presentation Skills, Communication & Interpersonal Skills, Effective Communication & Influencing Skills, Effective Business Writing Skills, Writing Business Documents, Business Writing (Memo & Report Writing), Controlling Your Time & Managing Stress, Crisis Management and Decision-Making Under Pressure; and Customer Experience, Service Excellence, and Negotiation Skills, Strategic Human Resources Management, Change Management and Organizational Development, Human Capital and Talent Management (succession planning, performance management, competency frameworks, and behavioral assessment), Strategic Planning and Execution, Project Risk Analysis & Risk Management, Global Diverse & Virtual Teams Operation, Exceeding Customer Expectations, Corporate Governance Best Practice, Business Performance Management & Improvement, Building Environment of Trust & Commitment, Win-Win Negotiation Strategies, Quality Improvement & Resource Optimization, Neuro Linguistic Programming (NLP), Personal Resilience Developing, Effective Role Modelling & Development, Managing Dynamic Work Environments, Organizational Development, Career Management, Situation & Behaviour Analysis, Interpersonal Motivation Skills, Inventory Management and Financial Administration. Further, he has also led or supported Training Needs Analyses (TNA), large-scale capability development programs, and leadership pipelines for technical, operational, and graduate employees.**

During his career life, Dr. Le Roux has gained his academic and field experience through his various significant positions and dedication as the **Training & Development General Manager, Departmental Head (Electrical), Project Manager, Account Manager, Commercial Sales Manager, Manager, Sales Engineer, Project Specialist, Psychology Practitioner, Senior Consultant/Trainer, Business Consultant, Assistant Chief Education Specialist, ASI Coordinator, Part-time Lecturer/Trainer, PMP & Scrum Trainer, Assessor & Moderator, Team Leader, Departmental Head, Senior HR Consultant, Senior Lecturer / Academic Supervisor, Technical Instructor/Qualifying Technician, Apprentice Electrician: Signals, International Trainer, and Part-Time Electrician** from various companies and universities such as the South African Railway (SAR), Department of Education & Culture, **ESKOM**, Logistic Technologies (Pty. Ltd), Human Development: Consulting Psychologies (HDCP) & IFS, Mincon, Eagle Support Africa, Sprout Consulting, UKZN, Grey Campus, Classis Seminars and CBM Training.

Dr. Le Roux has a **PhD in Leadership in Performance & Change**, a **Master's degree in Human Resource Management**, a **Bachelor's degree (with Honours) in Industrial Psychology**, a National Higher Diploma and a National Technical Diploma in **Qualified Electrical & Mechanical Engineering** from **Germiston College, South Africa**. Further, he is a **Certified Project Management Professional (PMP)**, a **PMI Authorized Training Partner (ATP) Instructor**, a **Certified Associate in Project Management (PMI-CAPM)**, a **Certified Scrum Master Trainer** by the VMedu, a **Certified Instructor/Trainer** and a **Certified Internal Verifier/Assessor/Trainer** by the **Institute of Leadership & Management (ILM)**. Moreover, he is a **Registered Industrial Psychologist** by the Health Professions Council of South Africa (HPCSA), a **Registered Educator** by the South African Council for Educators (SACE) and a **Registered Facilitator, Assessor & Moderator** with Education, Training and Development Practices (ETDP) SETA. He has further delivered numerous trainings, courses, seminars, conferences and workshops globally.



### **Training Methodology**

Our courses employ an interactive, learner-centred methodology that integrates theoretical knowledge with practical application. The training is delivered through a suitable combination of some or all of the following methods, selected according to the course content and learning objectives:

- Instructor-led presentations and facilitated discussions
- Practical workshops and participant presentations
- Hands-on exercises and real-world case studies
- Equipment demonstrations and technical drawings
- Hardware- and software-based simulations
- Gamification & Role Play in soft-skills courses only
- Virtual Reality (VR) and Augmented Reality (AR)
- Instructional videos and other relevant training resources

This blended approach encourages active participation, strengthens practical skills and supports the effective application of acquired knowledge in the workplace.

### **Learning Design & Customization**

This course can be customized to the exact requirements of clients. Haward Technology is so proud of our huge capabilities in tailoring our courses to the training needs of our valued clients.

### **Course Program**

The following program is planned for this course. However, the course instructor(s) may modify this program before or during the course for technical reasons with no prior notice to participants. Nevertheless, the course objectives will always be met:

#### **Day 1: Sunday, 27<sup>th</sup> of September 2026**

|             |                                                                                                                                                |
|-------------|------------------------------------------------------------------------------------------------------------------------------------------------|
| 0730 – 0800 | Registration & Coffee                                                                                                                          |
| 0800 – 0815 | Welcome & Introduction                                                                                                                         |
| 0815 – 0830 | <b>PRE-TEST</b>                                                                                                                                |
| 0830 – 1000 | <b>Project Risk Management</b><br>Introduction-Definitions • Risk Management Properties • Success of Risk Management                           |
| 1000 – 1015 | Break                                                                                                                                          |
| 1015 – 1200 | <b>Project Risk Management (cont'd)</b><br>Definition of Project Risk • Exercise: Issue or Risk • Risk Properties • Stakeholder Risk Attitudes |
| 1200 – 1300 | Lunch                                                                                                                                          |
| 1300 – 1400 | <b>Project Risk Management (cont'd)</b><br>Iterative Process • Risk Process Flow • Communication • Responsibility for Project Risk Management  |
| 1400 – 1415 | Break                                                                                                                                          |
| 1415 – 1650 | <b>Project Risk Management Processes</b><br>Project Risk Management & Project Management • All Projects Are Uncertain • The Processes          |
| 1650 – 1700 | <b>Distribute Homework &amp; Recap</b>                                                                                                         |
| 1700        | End of Day One                                                                                                                                 |



**Day 2: Monday, 28<sup>th</sup> of September 2026**

|             |                                                                                                                                                                                                                                                                                                                                                                                     |
|-------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 0730 – 0800 | <b>Review of Day 1 &amp; Homework Answers</b>                                                                                                                                                                                                                                                                                                                                       |
| 0800 – 1000 | <b>Plan Risk Management</b><br>Plan Risk Management Inputs • Inputs of This Process • Project Management Plan • Project Charter • Stakeholder Register • Enterprise Environmental Factors • Organizational Process Assets • Organization Risk • Example-Risk Appetite • Example-Risk Tolerance • Risk Appetite-Risk Tolerance                                                       |
| 1000 – 1015 | Break                                                                                                                                                                                                                                                                                                                                                                               |
| 1015 – 1200 | <b>Plan Risk Management (cont'd)</b><br>Organization Risk • Plan Risk Management- Inputs • Tools & Techniques for Plan Risk Management • Creating the Risk Management Plan • Exam Spotlight • Risk Categories • Risk Breakdown Structure (RBS) • Defining Probability & Impact • Probability & Impact Matrix • Recap the Steps for Risk Management Plan                             |
| 1200 – 1300 | Lunch                                                                                                                                                                                                                                                                                                                                                                               |
| 1300 – 1400 | <b>Identifying Potential Risk</b><br>Identifying Potential Risk Process • Identifying Potential Risk • Identifying Risks Inputs • Stakeholder Register • Organizational Process Assets • Tools & Techniques for Identifying Risks • Documentation Reviews • Information Gathering • Brainstorming • Nominal Group Technique • Delphi Technique • Interviewing • Root Cause Analysis |
| 1400 – 1415 | Break                                                                                                                                                                                                                                                                                                                                                                               |
| 1415 – 1650 | <b>Identifying Potential Risk (cont'd)</b><br>Checklist Analysis • Assumptions Analysis • Diagramming Techniques • Flow Chart Diagram • Influence Diagramming • Strengths, Weaknesses, Opportunities & Threats (SWOT) • Expert Judgment • Identify Risks Outputs • List of Identified Risks • List of Potential Responses • Triggers                                                |
| 1650 – 1700 | <b>Distribute Homework &amp; Recap</b>                                                                                                                                                                                                                                                                                                                                              |
| 1700        | End of Day Two                                                                                                                                                                                                                                                                                                                                                                      |

**Day 3: Tuesday, 29<sup>th</sup> of September 2026**

|             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |
|-------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 0730 – 0800 | <b>Review of Day 2 &amp; Homework Answers</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |
| 0800 – 1000 | <b>Perform Qualitative Risk Analysis Process</b><br>Process Overview • Perform Qualitative Risk Analysis Inputs • Tools & Techniques for Perform Qualitative Risk Analysis • Risk Probability & Impact Assessment • Probability • Impact                                                                                                                                                                                                                                                                                                                                                        |
| 1000 – 1015 | Break                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 1015 – 1200 | <b>Perform Qualitative Risk Analysis Process (cont'd)</b><br>Risk Impact • Probability & Impact Matrix • Risk Data Quality Assessment • Risk Urgency Assessment • Expert Judgment • Ranking Risks in the Risk Register                                                                                                                                                                                                                                                                                                                                                                          |
| 1200 – 1300 | Lunch                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
| 1300 – 1400 | <b>Perform Quantitative Risk Analysis Process</b><br>Perform Quantitative Risk Analysis Process • Process Overview • Perform Quantitative Risk Analysis Process • Tools & Techniques for Perform Quantitative Risk Analysis • Data-Gathering & Representation Techniques • Interviewing • Probability Distributions • Quantitative Risk Analysis & Modeling Techniques • Sensitivity Analysis • Expected Monetary Value (EMV) Analysis • Decision Tree Analysis • Modeling & Simulation • Simulation Techniques • Exam Spotlight • Expert Judgment • Perform Quantitative Risk Analysis Outputs |



|             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |
|-------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1400 – 1415 | Break                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |
| 1415 – 1650 | <b>Perform Quantitative Risk Analysis Process (cont'd)</b><br>Confidence Levels• Prioritized List of Quantified Risks• Trends in Perform Quantitative Risk Analysis Results• Formulas• Planned Value – Actual Cost-Earned Value• Cost Variance - Schedule Variance• Cost Variance• CPI-SPI• Cumulative CPI & SPI• Forecasting Formulas• Budget at Completion (BAC)• EAC Forecast for Etc Work Performed• The EAC Formula• To-Complete Performance Index (TCPI)• Variance Analysis |
| 1650 – 1700 | <b>Distribute Homework &amp; Recap</b>                                                                                                                                                                                                                                                                                                                                                                                                                                            |
| 1700        | End of Day Three                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |

**Day 4: Wednesday, 30<sup>th</sup> of September 2026**

|             |                                                                                                                                                                                                                                                                                                |
|-------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 0730 – 0800 | <b>Review of Day 3 &amp; Homework Answers</b>                                                                                                                                                                                                                                                  |
| 0800 – 1000 | <b>Plan Risk Responses Process</b><br>Plan Risk Responses Process• Overview of the Process• Exam Spotlight• Tools & Techniques for Plan Risk Responses• Strategies for Negative Risks or Threats • Avoid• Transfer• Mitigate • Accept • Strategies for Positive Risk or Opportunities• Exploit |
| 1000 – 1015 | Break                                                                                                                                                                                                                                                                                          |
| 1015 – 1200 | <b>Plan Risk Responses Process (cont'd)</b><br>Share• Enhance• Contingency Planning• Plan Risk Responses Outputs• Project Management Plan Updates • Project Documents Updates• Project Management Plan Updates• Project Documents Updates• Risk Register• Risk Register Contents               |
| 1200 – 1300 | Lunch                                                                                                                                                                                                                                                                                          |
| 1300 – 1400 | <b>Plan Risk Responses Process (cont'd)</b><br>Plan Risk Responses Process• Overview of the Process• Exam Spotlight• Tools & Techniques for Plan Risk Responses                                                                                                                                |
| 1400 – 1415 | Break                                                                                                                                                                                                                                                                                          |
| 1415 – 1615 | <b>Plan Risk Responses Process (cont'd)</b><br>Strategies for Negative Risks or Threats • Avoid • Transfer • Mitigate                                                                                                                                                                          |
| 1650 – 1700 | <b>Distribute Homework &amp; Recap</b>                                                                                                                                                                                                                                                         |
| 1700        | End of Day Four                                                                                                                                                                                                                                                                                |

**Day 5: Thursday, 01<sup>st</sup> of October 2026**

|             |                                                                                                               |
|-------------|---------------------------------------------------------------------------------------------------------------|
| 0730 – 0800 | <b>Review of Day 4 &amp; Homework Answers</b>                                                                 |
| 0800 – 1000 | <b>Control Risks</b><br>The Control Risks Process • Monitoring & Controlling Risk • Overview of Process       |
| 1000 – 1015 | Break                                                                                                         |
| 1015 – 1200 | <b>Control Risks (cont'd)</b><br>Control Risks Inputs • Control Risks Tools & Techniques • Risk Re-Assessment |
| 1200 – 1300 | Lunch                                                                                                         |
| 1300 – 1330 | <b>Control Risks (cont'd)</b><br>Risk Audits • Variance & Trend Analysis • Technical Performance Measurement  |




|             |                                                                                                                                                                      |
|-------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1330 – 1345 | Break                                                                                                                                                                |
| 1345 – 1615 | <b>Control Risks (cont'd)</b><br><i>Control Risks Outputs • Change Requests • Project Documents Updates</i>                                                          |
| 1615 – 1630 | <b>Course Conclusion</b><br><i>Using this Course Overview, the Instructor(s) will Brief Participants about the Course Topics that were Covered During the Course</i> |
| 1630 – 1645 | <b>POST-TEST</b>                                                                                                                                                     |
| 1645 – 1700 | <i>Presentation of Course Certificates</i>                                                                                                                           |
| 1700        | <i>End of Course</i>                                                                                                                                                 |

### **MOCK Exam**

Upon the completion of the course, participants have to sit for a MOCK Examination similar to the exam of the Certification Body through Haward's Portal. Each participant will be given a username and password to log in Haward's Portal for the MOCK exam during the 60 days following the course completion. Each participant has only one trial for the MOCK exam within this 60-day examination window. Hence, you have to prepare yourself very well before starting your MOCK exam as this exam is a simulation to the one of the Certification Body.

### **Book(s)**

As part of the course kit, the following e-books will be given to all participants:

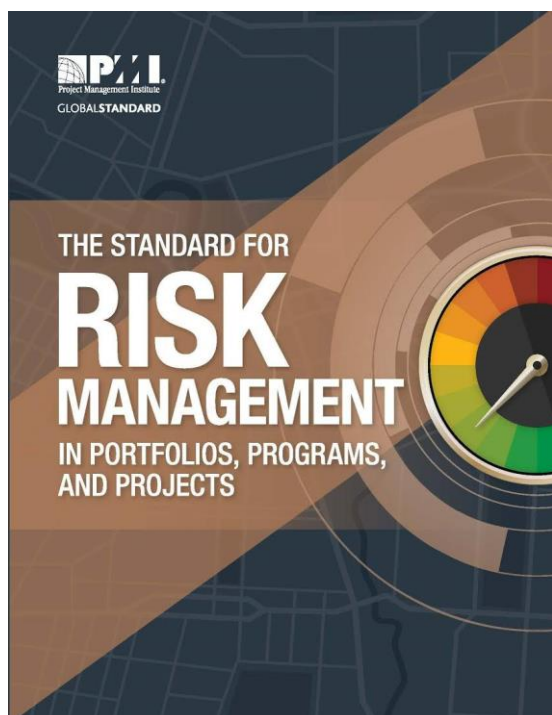


**Title:** The Standard for Risk Management in Portfolios, Programs and Projects  
**ISBN:** 978-1628255652  
**Author:** Project Management Institute  
**Publisher:** Project Management Institute




**Title:** Practice Standard for Project Risk Management  
**ISBN:** 978-9387486812  
**Author:** PMI  
**Publisher:** PMI

### Software Tools Demonstration


Practical sessions will be demonstrated through software tools during the course for delegates. Delegates will have an opportunity to understand the exercises using the “Mindview Software”, “Visio Software”, “ChatGPT” and “PMI Infinity”.

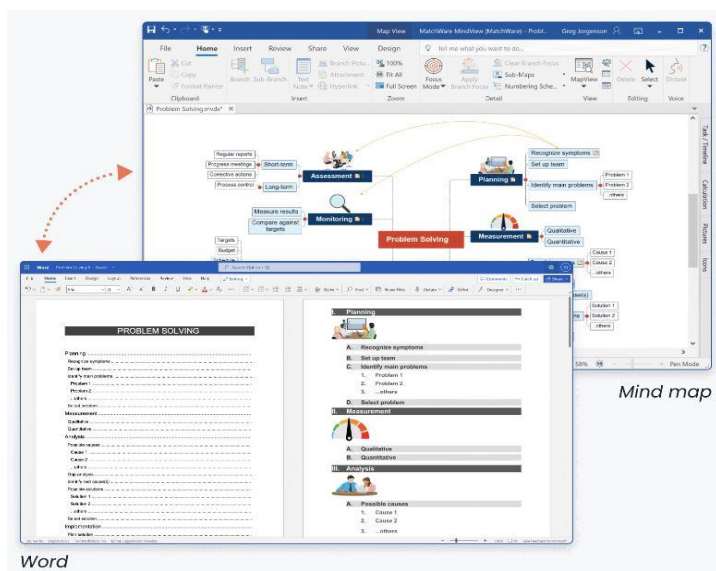


### Mindview Software

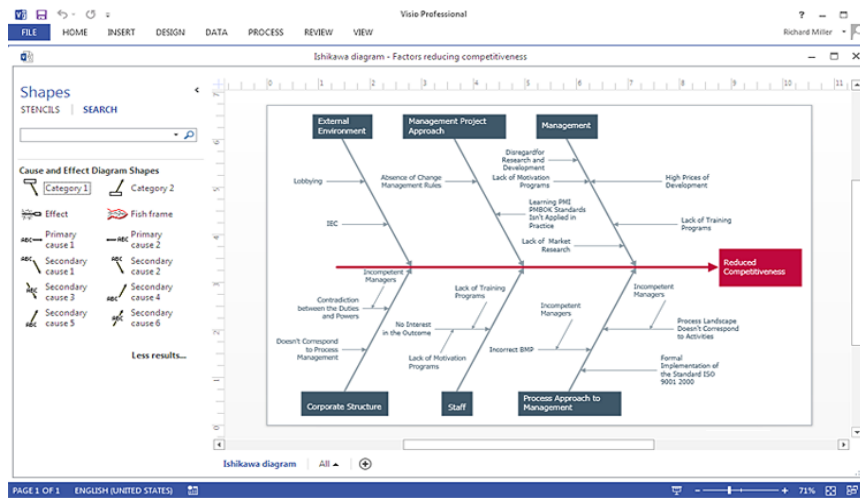

## Visio Software

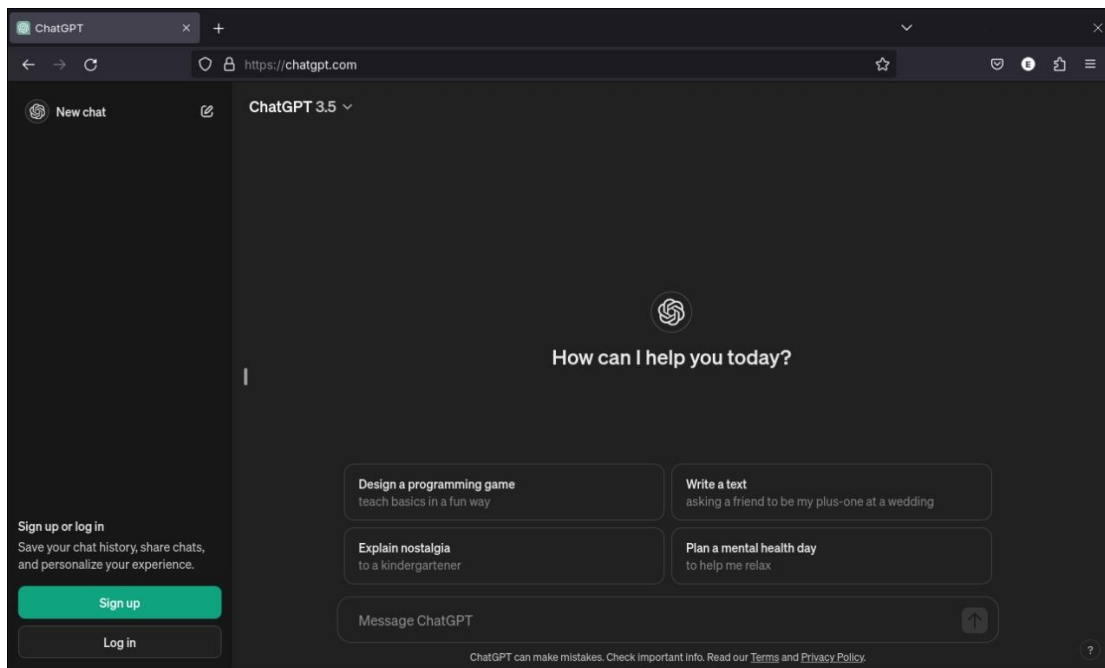

## ChatGPT Software

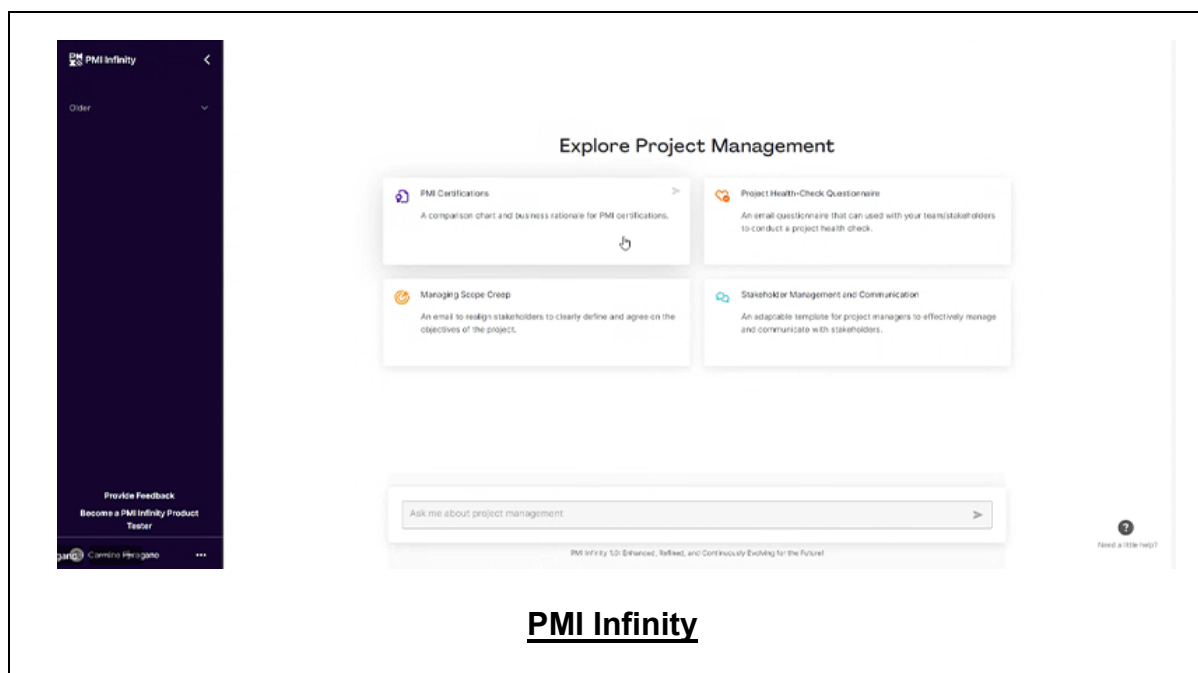

### **Course Coordinator**

Mari Nakintu, Tel: +971 2 30 91 714, Email: [mari1@haward.org](mailto:mari1@haward.org)
