

<u>COURSE OVERVIEW PE0248</u> <u>Process Plant Shutdown, Turnaround, Troubleshooting, Critical</u> <u>Activities, Isolation, Start Up & Commissioning</u>

Course Title

Process Plant Shutdown, Turnaround, Troubleshooting, Critical Activities, Isolation, Start Up & Commissioning

Course Date/Venue

February 02-06, 2025/Meeting Plus 5, City Centre Rotana Doha, Doha, Qatar

Course Reference PE0248

Course Duration/Credits Five days/3.0 CEUs/30 PDHs



Course Description







This practical and highly-interactive course includes various practical sessions and exercises. Theory learnt will be applied using our state-of-the-art simulators.

The process industry is losing over a billion dollars of profits a year due to poor shutdown and startup results. The majority of shutdown and startup lacked strategic focus and front-end planning. In addition, shutdown & startup teams lacked leadership and were understaffed. The major negative factor is the growing gap between higher shutdown performance expectations and rapidly shrinking qualified resources to manage the shutdowns. As a result, the planning effort not only starts late, but it is also ineffective, and typically does not contribute in the shutdown success.

This course is designed to bridge the abovementioned gap. It will provide participants with enough knowledge and skills to understand the purpose of the shutdown, to properly plan and manage the shutdown, and to achieve exponential results of their shutdown project. The course will teach participants how to establish a systematic shutdown management processes and procedures that incorporate the best shutdown practices, planning techniques and execution strategies.



PE0248 - Page 1 of 10





The course will cover the emerging industry trends, shutdown and startup benchmarking and the challenges to consistently achieve pacesetter results on plant shutdowns and startups. We will teach you how to fairly balance your business, marketing and financial goals with your plant needs for mechanical integrity and operational reliability. We will show you how to focus on risk areas, early work scope definition, high-performance initiatives, the assignment of qualified staff and the best practice contracting strategy.

The course will provide participants with a complete and up-to-date overview of the start-up of Process plants. It will also cover the troubleshooting of the start-up process. Upon the successful completion of this course, each participant will gain enough skills to anticipate and avoid problems associated with such start-up processes. Further, this course will provide participants with a satisfactory understanding of the organizational issues, estimation of required resources, CPM planning, mechanical integrity, troubleshooting, start-up operations, technical inspection, instrumentation/control systems, HSE and much other necessary knowledge associated with the process plant start-up. Actual case studies from around the world will be demonstrated to highlight the topics discussed.

Course Objectives

Upon the successful completion of this course, each participant will be able to:-

- Apply systematic techniques in process plant shutdown, turnaround, troubleshooting, critical activities, isolation, start-up and commissioning
- Compile and define the scope of work ad budget as well as operate and maintain inputs, identify pre-shutdown and start-up work and validate the work
- Illustrate the structure of shutdown including planning processes and their application
- Recognize shutdown team, materials and equipment
- Carryout shutdown organising, shutdown documentation, procurement and handover
- Execute shutdown and review feedback
- Control shutdown, apply starting up and handover and discuss health, safety and environment
- Employ process plant start-up, start-up operations, start-up progress monitoring and control
- Discuss instrumentation and control systems as well as apply performance and acceptance testing and preliminary tests
- Troubleshoot and solve problem in a professional manner
- Carryout change management covering the implementation of change, operational techniques and post commissioning audit



PE0248 - Page 2 of 10





Exclusive Smart Training Kit - H-STK[®]



Participants of this course will receive the exclusive "Haward Smart Training Kit" (**H-STK**[®]). The **H-STK**[®] consists of a comprehensive set of technical content which includes **electronic version** of the course materials conveniently saved in a **Tablet PC**.

Who Should Attend

This course provides a complete and up-to-date overview of the process plant shutdown and start-up for those involved in the shutdown and start-up operations of a process plant. This includes refinery process engineers, team leaders, project managers, section heads, plant supervisors, refinery maintenance engineers, refinery maintenance supervisors, refinery maintenance planners, maintenance operations personnel, operational staff and contractor personnel involved in the shutdown and start-up process. Mechanical, electrical, instrumentation and control engineers and operators who are involved in process plant shutdown and start-up will definitely benefit from this course.

Training Methodology

All our Courses are including Hands-on Practical Sessions using equipment, State-of-the-Art Simulators, Drawings, Case Studies, Videos and Exercises. The courses include the following training methodologies as a percentage of the total tuition hours: -

- 30% Lectures
- 20% Practical Workshops & Work Presentations
- 30% Hands-on Practical Exercises & Case Studies
- 20% Simulators (Hardware & Software) & Videos

In an unlikely event, the course instructor may modify the above training methodology before or during the course for technical reasons.

Course Fee

US\$ 6,000 per Delegate. This rate includes H-STK[®] (Haward Smart Training Kit), buffet lunch, coffee/tea on arrival, morning & afternoon of each day.

Accommodation

Accommodation is not included in the course fees. However, any accommodation required can be arranged at the time of booking.



PE0248 - Page 3 of 10





Course Certificate(s)

Internationally recognized certificates will be issued to all participants of the course who completed a minimum of 80% of the total tuition hours.

Certificate Accreditations

Certificates are accredited by the following international accreditation organizations: -

• **BAC**

British Accreditation Council (BAC)

Haward Technology is accredited by the **British Accreditation Council** for **Independent Further and Higher Education** as an **International Centre**. BAC is the British accrediting body responsible for setting standards within independent further and higher education sector in the UK and overseas. As a BAC-accredited international centre, Haward Technology meets all of the international higher education criteria and standards set by BAC.

• The International Accreditors for Continuing Education and Training (IACET - USA)

Haward Technology is an Authorized Training Provider by the International Accreditors for Continuing Education and Training (IACET), 2201 Cooperative Way, Suite 600, Herndon, VA 20171, USA. In obtaining this authority, Haward Technology has demonstrated that it complies with the **ANSI/IACET 2018-1 Standard** which is widely recognized as the standard of good practice internationally. As a result of our Authorized Provider membership status, Haward Technology is authorized to offer IACET CEUs for its programs that qualify under the **ANSI/IACET 2018-1 Standard**.

Haward Technology's courses meet the professional certification and continuing education requirements for participants seeking **Continuing Education Units** (CEUs) in accordance with the rules & regulations of the International Accreditors for Continuing Education & Training (IACET). IACET is an international authority that evaluates programs according to strict, research-based criteria and guidelines. The CEU is an internationally accepted uniform unit of measurement in qualified courses of continuing education.

Haward Technology Middle East will award **3.0 CEUs** (Continuing Education Units) or **30 PDHs** (Professional Development Hours) for participants who completed the total tuition hours of this program. One CEU is equivalent to ten Professional Development Hours (PDHs) or ten contact hours of the participation in and completion of Haward Technology programs. A permanent record of a participant's involvement and awarding of CEU will be maintained by Haward Technology. Haward Technology will provide a copy of the participant's CEU and PDH Transcript of Records upon request.



PE0248 - Page 4 of 10





Course Instructor(s)

This course will be conducted by the following instructor(s). However, we have the right to change the course instructor(s) prior to the course date and inform participants accordingly:



Dr. Faysal Eliyan, PhD, MSc, BSc, is a **Senior Engineer** with extensive years of experience within the **Oil & Gas**, **Petroleum** and **Refinery** industries. His expertise widely covers in the areas of **Process Plant** Equipment, **Process Equipment Design**, Sizing, Selection, Applications & Troubleshooting, **Process Plant Optimization** Technology & Continuous Improvement, **Plant Operation**, **Troubleshooting & Processing**, **Plant Layout Optimization**, **Concrete Structural Design**, **Concrete Maintenance & Reliability Analysis**, **Civil Engineering** Drawings, Standards & Codes,

Civil Engineering Design, Petrochemical Plant Structure Design & Remediation, Elements of Applied Civil Engineering, Dynamic Analysis of Rotating Equipment Foundations & Structural Steel Piperacks, Concrete & Structural Steel Design, Steel Structural Structure Design, Advanced **Building Construction Technology**, Engineering Techniques, Structural Renovation of Buildings, Earthwork & Structural Maintenance, Surface Drainage, Drainage System, Building Envelopes & Finishes, Landscaping & Roofing System, Seismic Design for Buildings, AutoCAD, Advanced Seismic & Wind Design of Reinforced Concrete, Structural Systems & Components, Design of Concrete Columns & Beam Frames, Design of Foundations & Equipment Footings, Maintenance of Concrete Structures, Structural Reliability Assessment, Codes & Structural Reliability, Probabilistic Evaluation of Existing Structures, Structural Steel, Precast Concrete and Reinforced Polymer Layered Steel. Further, he is also well-versed in Gas Turbines, Steam Turbines, Heat Exchangers Inspection, Testing & Overhaul Cleaning, Heating, Ventilation & Air Conditioning (HVAC), Fans & Blowers, Heaters & Boilers, Compressors, Maintenance Planning & Scheduling, Pumps & Compressors Operation & Maintenance, Valves Technology Selection, Installation & Troubleshooting, Cooling Towers, Rotating Equipment, Turbomachinery, Condition Monitoring & Diagnostics, Hydraulic & Pneumatic Systems Maintenance & Troubleshooting, Piping Systems, Corrosion Control & Materials Selection in Oil and Gas and Water Systems, Machinery Alignment & Balancing, Maintenance Management, Operational Problems & Failure Analysis, Energy Performance Assessment of Powerplants, Plant Operations, Project Management, Six Sigma and Health, Safety & Environment.

During his career life, Dr. Faysal has gained his practical and field experience through his various significant positions and dedication as the Assistant Professor, Senior Consultant, Laboratory Instructor, Lecturer, Tutor, Mentor, Advisor, Trainer, Engineering Manager, Senior Engineer, Senior Project Engineer, Engineer and Adjudicator from various institutions and universities such as the Community College of Qatar, American University of the Middle East, McMaster University, The University of British Columbia, The University of British Columbia, Qatar University and General Electric, just to name a few.

Dr. Faysal has PhD, Master and Bachelor degrees in Engineering from the University of British Columbia (Canada). He is a Certified Instructor/Trainer, a member of the Chamber of Civil Engineers, Structural Stability Research Council, American Institute of Steel Construction and American Society of Civil Engineers (ASCE), USA. He also published numerous books, researches and scientific papers and received several awards and recognitions for Journal of Materials Engineering and Performance and has further delivered numerous trainings, courses, seminars, workshops and conferences internationally.



PE0248 - Page 5 of 10





Course Program

The following program is planned for this course. However, the course instructor(s) may modify this program before or during the course for technical reasons with no prior notice to participants. Nevertheless, the course objectives will always be met:

Day 1:	Sunday, 02 nd of February 2025
0730 – 0800	Registration & Coffee
0800 - 0815	Welcome & Introduction
0815 - 0830	PRE-TEST
0830 - 0930	Introduction to ShutdownCompiling & Defining the Scope of Work and BudgetOperations &Maintenance InputsKickoff Meeting Agenda - Structured Group InterviewsIdentifying Pre-Shutdown & Start-up WorkValidating the Work
0930 - 0945	Break
0945 – 1100	Structure of the ShutdownPlanning Lead Time - Planning Phase is Actually a Project on its OwnProject Work Hours and Shifts• Project Charter and Scope Control• RisksAssessment• Quality Control Requirements• Checklists and Action ItemLists• Class Task
1100 – 1215	Planning Processes & their ApplicationThe Planning Tasks CycleWork Breakdown Structure, OrganizationBreakdown StructureActivity ListsActivity Information Determination-Duration, Resources, CostsDealing with Uncertainty in Job EstimatesClass Tasks
1215 – 1230	Break
1230 - 1420	<i>Shutdown Team, Materials & Equipment</i> Organising the Shutdown Project Team–Selecting the Manager • Organising Contracts and Procurement • Tracking Shutdown Materials • Coordinating Support Equipment
1420 - 1430	Recap Using this Course Overview, the Instructor(s) will Brief Participants about the Topics that were Discussed Today and Advise Them of the Topics to be Discussed Tomorrow
1430	Lunch & End of Day One

Day 2:	Monday, 03 rd of February 2025
0730 -0930	Organising Shutdown
	Organising the Shutting Down Meeting • Organising on Site Logistics •
	Organising Contract Work – Shifts, Labour and Technical Support
0930 - 0945	Break
0945 - 1100	Organising Shutdown (cont'd)
	Organising Tasks • Class Tasks
1100 - 1215	Shutdown Documentation, Procurement & Handover
	Documentation Needed & its Organisation • Organising the Store &
	Procurement Processes (Before & During)
1215 – 1230	Break



PE0248 - Page 6 of 10





1230 - 1420	Shutdown Documentation, Procurement & Handover (cont'd)Organising Progress FeedbackOrganising Start-up and Handover WorkPackages
1420 – 1430	Recap Using this Course Overview, the Instructor(s) will Brief Participants about the Topics that were Discussed Today & Advise Them of the Topics to be Discussed Tomorrow
1430	Lunch & End of Day Two

Day 3:	Tuesday, 04 th of February 2025
0730 - 0930	Shutdown Execution & Feedback
	Feedback Methods & Documentation • Meetings • Materials Management
	• Accounting – Time and Materials Systems for Feedback • Timeous
	Staging Quality, Safety & Activity Completion Class Tasks
0930 - 0945	Break
	Shutdown Execution & Feedback (cont'd)
0945 - 1100	Accounting – Time & Materials Systems for Feedback • Timeous Staging •
0545 - 1100	Tracking Shutdown Materials
	<i>Quality, Safety and Activity Completion</i> • <i>Class Tasks</i>
1100 - 1215	Control of Shutdown
	Methods of Control • Time Control from Feedback • Money Control from
	Feedback • Class Tasks
1215 - 1230	Break
1230 - 1420	Control of Shutdown (cont'd)
	Scope Change & Impact Control • Project Acceleration • Contractor
	Controls & Safety Control
1420 - 1430	Recap
	Using this Course Overview, the Instructor(s) will Brief Participants about the
	<i>Topics that were Discussed Today & Advise Them of the Topics to be Discussed</i>
	Tomorrow
1430	Lunch & End of Day Three

Day 4:	Wednesday, 05 th of February 2025
0730 -0830	Starting Up & Handover
	Schedules & Checklists • Completion Sign off Certificates • Payment
	Certificates (as Applicable) • Accounting Reports • Payment of Contractors
0830 - 0930	Health, Safety & Environment
	Hazard & Operability Analysis (HAZOP) • Hazard Analysis (HAZAN) •
	Process Safety Management (PSM) • Root Cause Analysis and Why Trees •
0030 - 0930	Risk Assessment • Hazard identification • Safety Training • HSE
	Problems and contingency plans • Safety Procedures and Implementation •
	Safety Manual
0930 - 0945	Break
	Process Plant Start-Up
0945 – 1100	Responsibilities & Authorities • Organizational Structure • Manpower &
	Staffing • Coordination Procedures • Leadership
1100 - 1215	Start-Up Operations
	Isolation of Vessels and Pipes • Types of Isolation • Initial Start-Up
	Activities • Steaming • Fuel Gas or Nitrogen Purge • Feed-in
1215 – 1230	Break
	Image: PE0248 - Page 7 of 10 Image: PE0248 - Page 7 Image: PE0248





1230 - 1330	Start-Up Progress Monitoring and ControlPlanning for SuccessSequence by UnitsSequence by SystemsRecovery from False Starts
1420 – 1430	Recap Using this Course Overview, the Instructor(s) will Brief Participants about the Topics that were Discussed Today & Advise Them of the Topics to be Discussed Tomorrow
1430	Lunch & End of Day Four

Day 5:	Thursday, 06 th of February 2025
0730 - 0930	Instrumentation & Control Systems
	Instrument Commissioning • Start-up Problems and Causes
0930 - 0945	Break
	Performance Trials
0945 – 1100	Performance and Acceptance Testing, Preliminary Tests • Performance Test
	Runs
	Troubleshooting & Problem Solving
1100 – 1215	<i>Identification of Problems & Priorities</i> • <i>Resource Allocation & Teamwork</i> •
1100 - 1213	Data Collection & Solution Selection • Troubleshooting Techniques • RCFA
	& RCM • Murphy's Law
1215 – 1230	Break
1230 - 1300	Change Management
	<i>Implementation of Change</i> • <i>Success Measures</i> • <i>Operational Techniques</i> •
	Post Commissioning Audit • Close-out Certificates
1345 - 1400	Course Conclusion
	Using this Course Overview, the Instructor(s) will Brief Participants about the
	Course Topics that were Covered During the Course
1400 - 1415	POST-TEST
1415 - 1430	Presentation of Course Certificates
1430	Lunch & End of Course




PE0248 - Page 8 of 10





Simulator (Hands-on Practical Sessions)

Practical sessions will be organized during the course for delegates to practice the theory learnt. Delegates will be provided with an opportunity to carryout various exercises using the "Simulis Thermodynamics", "ProPhyPlus", "ProSim Ternary Diagram", "Simulis Conversions" simulators and "ASPEN HYSYS" simulator.

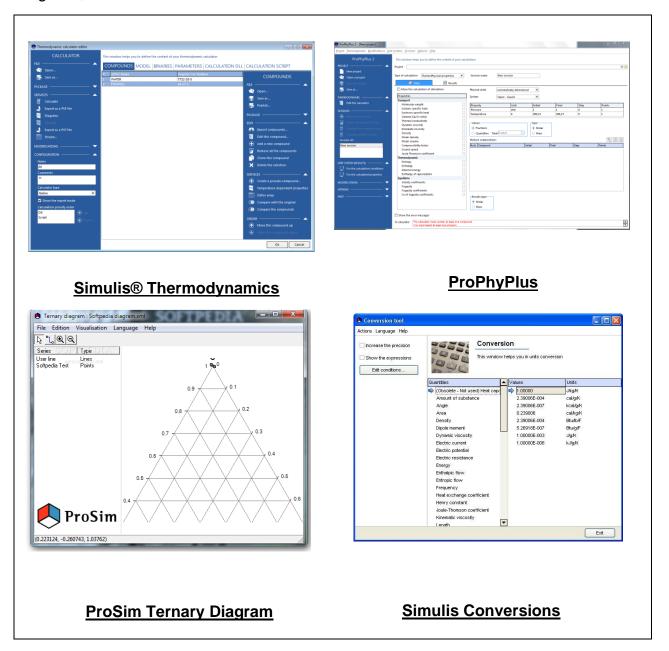




PE0248 - Page 9 of 10





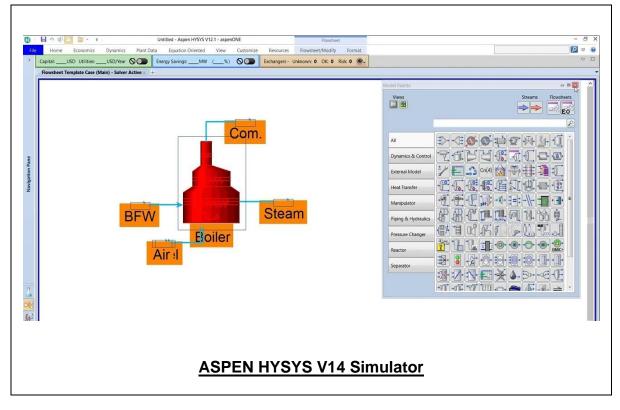

Course Coordinator

Reem Dergham, Tel: +974 4423 1327, Email: reem@haward.org



PE0248 - Page 10 of 10

